

Dam: Shannipo

Country: China

River: Beipan

26°14'12.82"N 104°49'26.4"E

26.236895 104.823997

Owner/Client: Guizhou Qianyuan Power Co. Ltd.

Designer/Engineer: Guiyang Hydropower Investigation, Design and Research Institute, CHECC

Contractor: Unknown

Purpose (code): H

Site start: 01.01.2009

RCC start: 01.01.2011

RCC completion: 31.12.2013

Site completion: 31.12.2015

Height (m): 119

Length (m): 205

Volume of RCC (m<sup>3</sup>x10<sup>3</sup>): 199

Total volume (m<sup>3</sup>x10<sup>3</sup>): 267

Reservoir capacity (m<sup>3</sup>x10<sup>6</sup>): 85

Upstream slope: curve

Forming of upstream face (code): (3')

Downstream slope: curve

Forming of downstream face (code): (3)

Spillway slope: ogee

Forming of spillway face (code): (3)

Depth of layers (mm): Unknown

Depth of lifts (mm): Unknown

Cement content (kg/m<sup>3</sup>): Unknown

Pozzolan content (kg/m<sup>3</sup>): Unknown

Code for pozzolan: Unknown

RCCDAM Unique Serial No.: RCCDAM0609

### Under Construction




RCCDAM0609UC

### Completed Dam



RCCDAM0609CD

### Google Earth

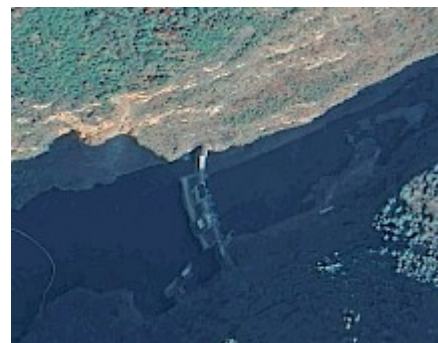

RCCDAM0609GE

# Guide to Abbreviations

## Purpose

- E Environmental
- F Flood control
- G Groundwater recharge
- H Flood control
- I Irrigation
- N Navigation
- P Pollution control
- R Recreation
- W Water supply

## Facing method

- (1) Traditional concrete against formwork
- (2) Traditional concrete against formwork with external geomembrane
- (3) RCC against formwork
- (4) RCC against formwork with external geomembrane
- (5) Traditional concrete against precast concrete panels
- (6) Traditional concrete against precast concrete panels with geomembrane
- (7) RCC against precast concrete panels
- (8) RCC against precast concrete panels with geomembrane
- (9) RCC against precast concrete panels with hot poured membrane
- (10) RCC against precast concrete blocks
- (11) Reinforced conventional concrete cast before RCC placement
- (12) Reinforced conventional concrete cast after RCC placement
- (13) Reinforced concrete cast against precast units or slip-formed facing elements
- (14) Slip-formed/extruded facing elements
- (15) RCC supported by fill shoulders
- (16) Mechanically compacted unformed face of RCC
- (17) Unformed face of RCC
  - ' GEVR/GE-RCC
  - \* Stepped face

## Pozzolans

- (-) No Pozzolan Used
- (C) High-lime flyash (ASTM Class C)
- (F) Low-lime flyash (ASTM Class F)
- (M) Milled sand
- (N) Natural pozzolan (ASTM Class N)
- (R) ROLAC (mixture of flyash and slag with or without limestone fines)
- (S) Ground-granulated blast-furnace slag
- (L) Mixture of GGBFS and limestone fines
